Tacoma Subaru Admin Extension

ID	Task Mode	Task Name
1		**Tacoma Subaru - Admin. Building Extension**
2		Contract
3		PreConstruction meeting
4		Submittals
5		Subcontracts
6		Mobilize
7		Temporary Fencing (Protective)
8		TESC (Erosion Control)
9		TESC Inspection
10		Utility Locate
11		Sawcutting
12		Demo Asphalt
13		Demo Stairs/Planter
14		Dig for Footing
15		Prep Subgrade
16		Form For Footings
17		Install Rebar
18		Inspection
19		Pour Footings
20		Form For Stem Wall
21		Install Rebar
22		Inspection
23		Pour Stem Wall
24		Cure Period (5 Days)
25		Backfill
26		Placement of Underground Power
27		Placement of Underground Plumbing
28		Capillary Break
29		Vapor Barrier
30		Rebar in Slab/ Tie In
31		Inspection
32		Pour Slab (w/ Stoop and Stairs)
33		Form For Stoop/Stairs
34		Install Rebar
35		Inspection
36		Interior Demolition
37		Demo Storefront w/ Windows
38		Construct Temp Wall
39		Framing For Walls Exterior
40		Framing for Interior Walls/Partitions/Pony Walls
41		Roof Framing and Sheathing
42		Roofing/Sheet Metal
43		Electrical Rough In
44		Electrical Rough In Inspection
45		HVAC Rough In
46		HVAC Inspection
47		Plumbing Rough In
48		Plumbing Inspection
49		Wall Framing Inspection
50		Insulation
51		Insulation Inspection
52		Soffit Framing
53		EIFS
54		Install Door Frames
55		Hang GWB
56		Tape and Texture
57		Paint Interior/Exterior
58		Installation of Handrail
59		Install Windows
60		Install Acoustical Ceiling Grid
61		Install Flooring
62		Casework
63		Plumbing Trim
64		HVAC Trim
65		Electrical Trim
66		Plumbing Inspection
67		HVAC Inspection
68		Electrical Inspection
69		Install Acoustical Tile
70		Building Final Inspection
71		Final Clean
72		Demobilize

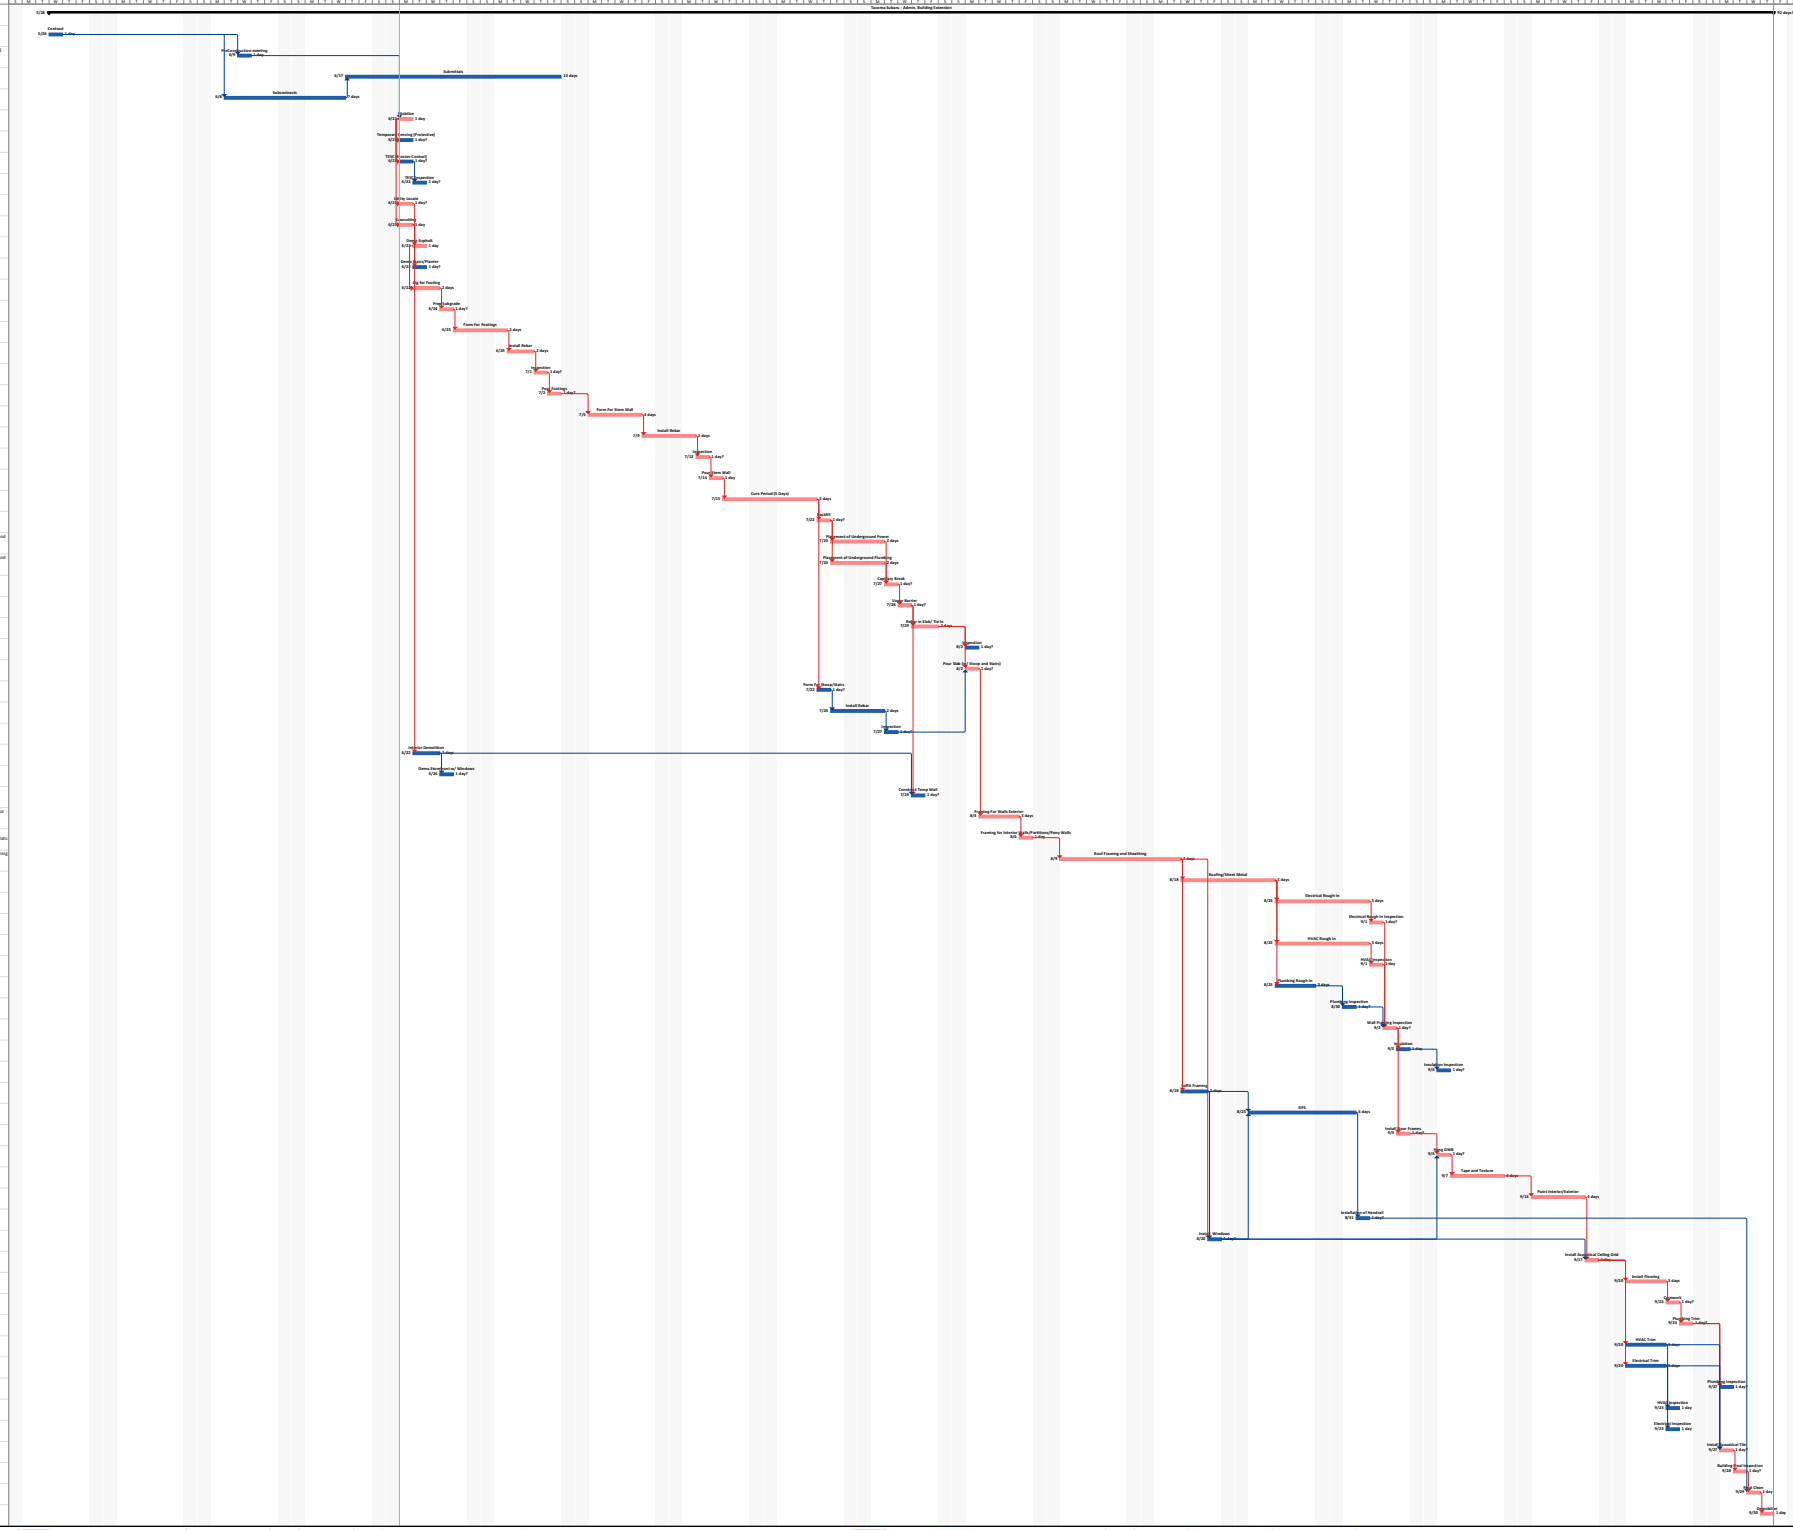

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Critical | Critical Split | Progress | Manual Progress
